

MEASURE E

Citizens Oversight Committee Quarterly Meeting

February 3, 2025

Board of Education

Lauren Brooks Jeff Kim Katie McEwen, President Connie Stone Cyril Yu



AGENDA

Budget

State Funding

Schedule

Project Updates

- Series 2021C (Series 3)
- Series 2023D (Series 4)







MEASURE E ORIGINAL BOND SERIES

- Original Measure E Bond capacity based on annual Assessed
 Valuation growth within the SFID of 3% 4.5% to be issued in four Series
 - Yielding projected project funding of \$250.8 Million up to \$319.0 Million
 - Measure E initial budget set at \$250.8 Million
- Annually review Assessed Valuation to determine growth and potential impact to bonding capacity
- Based on growth within the SFID, assumptions increased to annual Assessed Valuation growth of 3.5%
 - Yielding projected project funding *now of \$306.0* Million up to \$319.0 Million
 - Increase number and frequency of Series from four to five



MEASURE E REVISED BOND SERIES


- Series 1 funds received October 26, 2016
- Series 2 funds received September 13, 2018
- Series 3 funds received April 7, 2021
- Series 4 Bond received October 25, 2023

2029 (Series 4) TOTAL	\$ 54.5M \$ 250.8M *	2024 (Series 4) 2028 (Series 5)	\$ 45.0M \$ 55.0M
2025 (Series 3)	\$ 49.4M \$ 54.5M	2021 (Series 3)	\$ 45.0M
2021 (Series 2)	\$ 51.9M	2018 (Series 2)	\$41.0M
2016 (Series 1)	\$ 95.0M	2016 (Series 1)	\$ 95.0M
<u>ORIGINAL (</u>	<u> 2016)</u>	<u>ISSUED/PROPC</u>)SED (2021)

ISSUED/CURRENT (2023) 2016 (Series 1) \$ 95.0M 2018 (Series 2) \$ 41.0M 2021 (Series 3) \$ 45.0M 2023 (Series 4) \$ 60.0M 2028 (Series 5) \$ 65.0M TOTAL \$306.0M*



MEASURE E FUNDING TIMELINE

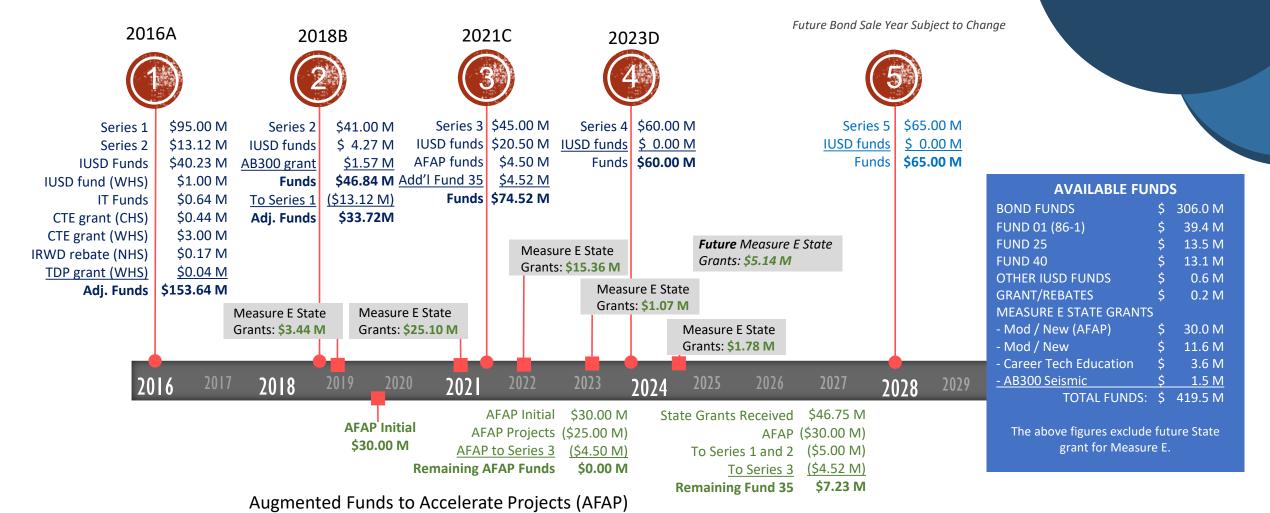



MEASURE E BUDGET VERSIONS 1 22

2b

3

Close

Construction

Cautana

Out

Master Plan Concept Design

Schematic` Design Design Devel. Constr. Docs.

Bid / Award

← Series 3

PRELIMINARY

- Master Plan (2015)
- Broad Scope (unit costs times sq. ft.)
- Soft Cost general percentage
- Schedules not defined

INITIAL

Series 4

- Concept Design Completion
- Refined Soft Costs based on project scope
- Escalation, project schedules defined

"REVISED" INITIAL

- Design Development Completion
- Architect / CM
 Cost Estimates

POST-BID

 Award of Construction Bids

FINAL

- Project Completion
- Contractor's Notice of Completion Filing and Final Payment of Purchase Orders

If cost estimate exceeds budget, identify Bid Alternates and potential work to defer until funding is available.

If bid(s) exceeds budget, identify work to defer until funding is available or identify additional funds.



MEASURE E BUDGET SUMMARY

								I	unds	s Available								Fi	unds Available Total	-	Project Costs	Sui	plus / Deficit by Year	(Cumulative Totals
	Bond Series or	[A]		[B]		[C]		[D]		[E]	[F]		[G]		[H]		[1]		[J]		JK)		[L]		[M]
Year	Fund Sources	Bonds	District		Receive CTE/A		State Grants Received from CTE/AB300 Programs Other Grants / Rebates		Ot	her Funds	Mea	tate Grants I sure E Buildi r AFAP / Addi (Fun	ng Pro itional d 35)	gram used Funding		Sum A thru I		xpenditures or roject Budget		[J-K]					
			Fun	nd 01 (CFD 86-1)	F	und 25		Fund 40		Fund 35)					AFAP		lditional s to Series								
2016	Series 1	\$ 108,115,495	\$ 23	3,000,000	\$ 12	2,231,276	\$	6,000,000	\$	3,439,400	\$ 219,031	\$	643,875	\$	-	\$	-	\$	153,649,077	\$	151,659,238	\$	1,989,839	\$	1,989,839
2018	Series 2	\$ 27,884,505	\$	-	\$ 1	,268,724	\$	3,000,000	\$	1,565,006	\$ -	\$	-	\$	-	\$	-	\$	33,718,235	\$	31,540,384	\$	2,177,851	\$	4,167,690
2019	AFAP	\$ -	\$	-	\$	-	\$	-	\$	-	\$ -	\$	-	\$ 2	5,500,000	\$	-	\$	25,500,000	\$	21,345,683	\$	4,154,317	\$	8,322,007
2021	Series 3	\$ 45,000,000	\$ 10	6,400,000	\$	-	\$	4,100,000	\$	-	\$ -	\$	-	\$	-	\$	9,021,669	\$	74,521,669	\$	86,842,308	\$ (12,320,639)	\$	(3,998,632)
2023	State Grants (remaining available)	\$ -	\$	-	\$	-	\$	-	\$	-	\$ -	\$	-	\$	-	\$	7,224,509	\$	7,224,509	\$	-	\$	7,224,509	\$	3,225,877
2023	Series 4	\$ 60,000,000	\$	-	\$	-	\$	-	\$	-	\$ -	\$	-	\$	-	\$	-	\$	60,000,000	\$	60,000,000	\$	-	\$	3,225,877
2028	Series 5	\$ 65,000,000	\$	-	\$	-	\$	-	\$	-	\$ -	\$	-	\$	-	\$	-	\$	65,000,000	\$	51,400,000	\$	13,600,000	\$	16,825,877
то	OTALS	\$ 306,000,000	\$ 3	9,400,000	\$ 13	3,500,000	\$	13,100,000	\$	5,004,406	\$ 219,031	\$	643,875	\$ 2	25,500,000	\$ 1	5,246,178	\$	419,613,490	\$	402,787,613	\$	16,825,877	\$	16,825,877



MEASURE E POST-BID BUDGET vs FINAL BUDGET

	Completed Projects	Pos	st-Bid Budget	F	inal Budget	 -Bid & Final get Variance
1	Bonita Canyon ES - Enclose Classrooms	\$	912,184	\$	868,451	\$ 43,733
2	College Park ES - Enclose Classrooms	\$	3,424,255	\$	3,248,271	\$ 175,984
3	Creekside HS - Expansion	\$	5,032,263	\$	4,843,117	\$ 189,146
4	Culverdale ES - Enclose Classrooms	\$	1,633,772	\$	1,601,117	\$ 32,655
5	Eastshore ES - Expansion	\$	6,132,736	\$	6,080,570	\$ 52,166
6	Greentree ES - Enclose Classrooms	\$	2,042,302	\$	1,913,892	\$ 128,410
7	Irvine HS - Modernization	\$	7,143,636	\$	6,922,265	\$ 221,371
8	Lakeside MS - Science Labs	\$	2,972,572	\$	2,892,181	\$ 80,391
9	Northwood HS - Field Improvements	\$	3,815,212	\$	3,692,908	\$ 122,304
10	Rancho San Joaquin MS - Science Labs	\$	5,680,277	\$	5,289,332	\$ 390,945
11	Santiago Hills ES - Enclose Classrooms	\$	1,498,668	\$	1,427,186	\$ 71,482
12	Sierra Vista MS - Science Lab	\$	4,871,155	\$	4,588,557	\$ 282,598
13	South Lake MS - Science Labs	\$	3,759,011	\$	3,557,805	\$ 201,206

				,		·	
14	Stone Creek ES - Enclose Classrooms/Expansion	\$	4,423,481	\$	4,295,488	\$	127,993
15	University HS - Modernization	\$	5,002,422	\$	4,628,058	\$	374,364
16	Venado MS - Science Labs	\$	5,318,603	\$	5,184,530	\$	134,073
17	Westwood Basics Interim	\$	509,966	\$	411,938	\$	98,028
18	Westpark ES - Modernization	\$	10,519,152	\$	10,634,410	\$	(115,258)
19	Brywood ES - Modernization	\$	10,678,948	\$	11,306,486	\$	(627,538)
20	Brywood ES - Music Classroom	\$	3,073,480	\$	2,919,341	\$	154,139
21	Meadow Park ES - Modernization	\$	13,056,650	\$	13,043,246	\$	13,404
22	Meadow Park ES - Music Classroom	\$	3,122,369	\$	2,984,289	\$	138,080
23	Springbrook ES - Modernization	\$	12,105,298	\$	11,965,170	\$	140,128
24	Springbrook ES - Music Classroom	\$	3,561,804	\$	3,318,008	\$	243,796
25	Woodbridge HS - Field Improvements	\$	2,974,100	\$	3,163,725	\$	(189,625)
26	Woodbridge HS - Performing Arts Center	\$	27,120,257	\$	28,881,980	\$	(1,761,723)
27	El Camino School - Interim Campus	\$	1,807,102	\$	1,260,683	\$	546,419
	TOTALS	\$1	152,191,674	\$1	150,923,004	\$	1,268,670

Percentage below Post-Bid Budget

0.83%






BUDGET CHANGE ORDERS

MEASURE E CHANGE ORDERS (SUMMARY)

"A 'change order' refers to an official change of any kind in the original scope of work or terms of a construction contract agreed to by the owner, contractor, and project designer." Associated General Contractors of America



	Final Change Order Percentages (All Series)												
	School Original Contract Final Contract Change Orders Change Order %												
1	Series 1 (complete)	\$	113,606,920	\$	113,852,871	\$	245,951	0.22%					
2	Series 2 (complete)	\$	19,978,401	\$	19,964,597	\$	(13,804)	-0.07%					
3	Series 3 (ongoing)	\$	36,770,073	\$	38,218,546	\$	1,448,473	3.94%					
4	AFAP (complete)	\$	13,267,744	\$	13,369,594	\$	101,850	0.77%					
	TOTALS \$ 183,623,138 \$ 185,405,608 \$ 1,782,470 0.												



MEASURE E FINAL CHANGE ORDERS (SERIES 1)

	Final Change Order Percentages (Series 1)																
	School	Orig	ginal Contract	Fir	nal Contract	Cha	ange Orders	Change Order %		School	Ori	ginal Contract	Fi	nal Contract	Cha	ange Orders	Change Order %
1	Bonita Canyon ES	\$	687,833	\$	661,920	\$	(25,913)	-3.77%	14	Westpark ES	\$	7,535,025	\$	7,612,852	\$	77,827	1.03%
2	College Park ES	\$	1,947,472	\$	1,997,707	\$	50,235	2.58%	15	Brywood ES - Mod	\$	8,022,047	\$	8,634,679	\$	612,632	7.64%
3	Culverdale ES	\$	1,004,045	\$	1,020,602	\$	16,557	1.65%	16	Brywood ES - Music	\$	2,842,214	\$	2,773,341	\$	(68,873)	-2.42%
4	Greentree ES	\$	1,263,711	\$	1,240,335	\$	(23,376)	-1.85%	17	Meadow Park ES - Mod	\$	9,640,387	\$	9,856,858	\$	216,471	2.25%
5	Santiago Hills ES	\$	1,053,407	\$	1,050,915	\$	(2,492)	-0.24%	18	Meadow Park ES - Music	\$	2,889,679	\$	2,838,289	\$	(51,390)	-1.78%
6	Stone Creek ES	\$	3,155,560	\$	3,113,229	\$	(42,331)	-1.34%	19	Eastshore ES	\$	4,522,529	\$	4,597,990	\$	75,461	1.67%
7	Northwood HS	\$	2,946,419	\$	3,055,203	\$	108,784	3.69%	20	Venado MS	\$	3,798,615	\$	3,813,274	\$	14,659	0.39%
8	Irvine HS	\$	4,704,255	\$	4,843,227	\$	138,972	2.95%	21	Creekside HS	\$	3,681,144	\$	3,598,072	\$	(83,072)	-2.26%
9	University HS	\$	3,533,004	\$	3,519,126	\$	(13,878)	-0.39%	22	Springbrook ES- Mod	\$	8,110,543	\$	8,413,410	\$	302,867	3.73%
10	Sierra Vista MS	\$	3,643,560	\$	3,526,896	\$	(116,664)	-3.20%	23	Springbrook ES- Music	\$	3,387,188	\$	3,245,008	\$	(142,180)	-4.20%
11	South Lake MS	\$	2,753,376	\$	2,688,937	\$	(64,439)	-2.34%	24	Woodbridge HS-Field Imp	\$	2,568,204	\$	2,651,706	\$	83,502	3.25%
12	Lakeside MS	\$	2,279,702	\$	2,214,866	\$	(64,836)	-2.84%	25	Woodbridge HS-PAC	\$	23,435,033	\$	22,782,163	\$	(652,870)	-2.79%
13	Rancho San Joaquin MS	\$	4,201,968	\$	4,102,266	\$	(99,702)	-2.37%		TOTALS	\$ 1	13,606,920	\$	113,852,871	\$	245,951	0.22%



MEASURE E FINAL CHANGE ORDERS (SERIES 2)

Final Change Order Percentages (Series 2)													
School Original Contract Final Contract Change Orders													
1	Bonita Canyon ES	\$	5,223,926	\$	5,197,335	\$	(26,591)	-0.51%					
2	Northwood ES	\$	5,436,042	\$	5,426,486	\$	(9,556)	-0.18%					
3	Turtle Rock ES	\$	4,122,526	\$	3,920,458	\$	(202,068)	-4.90%					
4	University Park ES	\$	5,195,907	\$	5,420,318	\$	224,411	4.32%					
TOTALS \$ 19,978,401 \$ 19,964,597 \$ (13,804)													



MEASURE E FINAL CHANGE ORDERS (SERIES 3)

Final Change Order Percentages (Series 3)

	School	Ori	ginal Contract	ı	Final Contract	Ch	ange Orders	Change Order %
1	South Lake MS - Mod	\$	5,367,388	\$	5,731,002	\$	363,614	6.77%
2	South Lake MS - Music	\$	2,300,392	\$	2,237,613	\$	(62,779)	-2.73%
3	Culverdale ESS- MPR/Nutr.	\$	10,465,926	\$	10,963,291	\$	497,365	4.75%
4	Greentree ES - MPR	\$	7,415,008	\$	7,764,733	\$	349,725	4.72%
5	Greentree ES - Interior	\$	2,059,325	\$	2,164,227	\$	104,902	5.09%
6	Santiago Hills ES - MPR	\$	7,470,690	\$	7,709,220	\$	238,530	3.19%
7	Santiago Hills ES - Interior	\$	1,691,344	\$	1,648,460	\$	(42,884)	-2.54%
8	Irvine HS - PAC				(closing out pro	ject)	
	TOTALS	\$	36,770,073	\$	38,218,546	\$	1,448,473	3.94%



MEASURE E FINAL CHANGE ORDERS (AFAP)

Final Change Order Percentages (AFAP)													
School Original Contract Final Contract Change Orders													
1	Canyon View ES	\$	2,828,297	\$	2,886,649	\$	58,352	2.06%					
2	Deerfield ES	\$	3,744,720	\$	3,774,694	\$	29,974	0.80%					
3	Oak Creek ES	\$	2,654,110	\$	2,594,372	\$	(59,738)	-2.25%					
4	Plaza Vista School	\$	4,040,617	\$	4,113,879	\$	73,262	1.81%					
TOTALS \$ 13,267,744 \$ 13,369,594 \$ 101,850													





BUDGET UPDATE BY SERIES

MEASURE E BUDGET ITERATIONS (SERIES 1)

Adjustment (10/26	/2016)	Adjustment (06	/05	/2018)	FIN	NAL			
Fund Source		Funding	Fund Source		Funding	Fund Source		Funding		
Bond Series 1	\$	95,000,000	Bond Series 1	\$	95,000,000	Bond Series 1	\$	95,000,000		
IUSD Funds	\$	29,600,000	IUSD Funds	\$	29,600,000	IUSD Funds	\$	28,331,276		
IUSD Funds 1st Adj.	\$ 6,800,000		IUSD Funds 1st Adj.	\$	6,800,000	IUSD Funds 1st Adj.	\$	6,800,000		
FUNI	DS \$	131,400,000	IUSD Funds 2nd Adj.	\$	5,100,000	IUSD Funds 2nd Adj.	\$	5,100,000		
			IUSD IT Infrastructure	\$	643,875	IUSD IT Infrastructure	\$	643,875		
			CTE Grant (CHS)	\$	348,920	CTE Grant (CHS)	\$	439,400		
			Bond Series 2	\$	13,115,495	Bond Series 2	\$	13,115,495		
			FUNDS	\$	150,608,290	IRWD Rebate (NHS)	\$	174,591		
						Fund 40 to WHS Field	\$	1,000,000		
						CTE Grant (WHS)	\$	3,000,000		

TDP Grant (WHS)

FUNDS \$



44,440

153,649,077

MEASURE E BUDGET ITERATIONS (SERIES 2)

Initial Budget (01/19/	(2019)	Adjustment	(12/01/2	2020)	FINAL					
Fund Source		Funding	Fund Source		Funding	Fund Source		Funding			
Bond Series 2	\$	41,000,000	Bond Series 2	\$	41,000,000	Bond Series 2	\$	41,000,000			
Bond Funds to Series 1	\$	(13,115,495)	Bond Funds to Series 1	\$	(13,115,495)	Bond Funds to Series 1	\$	(13,115,495)			
IUSD Funds	\$	-	IUSD Funds	\$	3,000,000	IUSD Funds	\$	4,268,724			
FUND)S \$	27,884,505	FUN	IDS \$	30,884,505	AB300 Grant (UPES)	\$	1,565,006			
						FUN	DS \$	33,718,235			



MEASURE E BUDGET ITERATIONS (SERIES 3)

Initial Budget (01/06	/2021)	Adjustment (06/02/2	2021)	Current (02/03/2025)					
Fund Source		Funding	Fund Source		Funding	Fund Source		Funding			
Bond Series 3	\$	30,800,000	Bond Series 3	\$	45,000,000	Bond Series 3	\$	45,000,000			
IUSD Funds	\$	23,500,000	IUSD Funds	\$	23,500,000	IUSD Funds	\$	23,500,000			
IUSD Funds to Series 2	\$	(3,000,000)	IUSD Funds to Series 2	\$	(3,000,000)	IUSD Funds to Series 2	\$	(3,000,000)			
FUNI)S \$	51,300,000	AFAP Funds	\$	4,500,000	Add'l AFAP Funds	\$	4,500,000			
			FUN	DS \$	70,000,000	Fund 35	\$	4,521,669			
						FUND)\$ \$	74,521,669			




MEASURE E BUDGET ITERATIONS (AFAP)

Initial Budget (11/19/2019)		
Fund 35	\$	30,000,000
	FUNDS \$	30,000,000

Current (02/03/2025)		
Fund 35	\$	30,000,000
AFAP Projects Budgeted	\$	(25,500,000)
AFAP Made Available to Series 3	\$	(4,500,000)
AFAP FUNDS	\$	-

No Changes (02/03/2025)





OFFICE OF PUBLIC SCHOOL CONSTRUCTION: STATE GRANTS

State Grants Received

State Grants Received from Proposition 51 Bond funds

STATE FUNDED PROJECTS (Prop. 51) – Measure E Only		
Site Name	Amount Received	
Creekside High School (Series 1 CTEFP: Const. Tech.)	\$439,400	
Woodbridge High School (Series 1 CTEFP: Perf. Arts)	\$3,000,000	
College Park ES (Series 1: MOD)	\$527,914	
Culverdale ES (Series 1: MOD)	\$784,679	
Santiago Hills ES (Series 1: MOD)	\$625,105	
Stone Creek ES (Series 1: MOD)	\$896,562	
Stone Creek ES (Series 1: NC)	\$727,603	
Irvine HS (Series 1: MOD)	\$4,256,129	
University HS (Series 1: MOD)	\$735,286	
Creekside HS (Series 1: NC)	\$1,166,945	
Sierra Vista MS (Series 1: NC)	\$1,671,605	

The State grants funds are through the State School Facility Program currently under Proposition 51.

STATE FUNDED PROJECTS – Measure E Only (Cont'd.)	
Site Name	Amount Received
South Lake MS (Series 1: NC)	\$919,005
Eastshore ES (Series 1: MOD)	\$757,980
Eastshore ES (Series 1: NC)	\$833,174
Venado MS (Series 1: NC)	\$2,249,063
Rancho San Joaquin MS (Series 1: MOD)	\$570,889
Rancho San Joaquin MS (Series 1: NC)	\$1,176,896
Springbrook ES (Series 1: MOD)	\$3,472,248
Westpark ES (Series 1: MOD)	\$3,729,015
Brywood ES (Series 1: MOD)	\$3,133,957
Woodbridge HS (Series 1: NC)	\$3,219,613
Springbrook ES (Series 1: NC)	\$1,211,516
Meadow Park ES (Series 1: NC)	\$1,358,675
Meadow Park ES (Series 1: MOD)	\$3,529,201
Brywood ES (Series 1: NC)	\$1,343,490
University Park ES (Series 2: MOD)	\$1,565,006
Bonita Canyon ES (Series 1: MOD)	\$334,581
Greentree ES (Series 1: MOD)	\$373,866
Lakeside MS (Series 1: MOD)	\$364,925
Turtle Rock ES (Series 2: NC)	\$1,776,256
Total State Funds Received	\$46,750,584



OFFICE OF PUBLIC SCHOOL CONSTRUCTION: STATE GRANTS

Step 1a: "Acknowledged" List

When no State Funding is available

- Project applications submitted beyond the Proposition 51 Bond Authority
- Subject to IUSD Board Resolution acknowledging exhaustion of funds
- Waiting for future State Bond (potentially in 2024)

Step 1b: "Workload" List

When State Funding is available

- Project applications submitted to OPSC, waiting for staff review
- ➤ Anticipate funding under Prop. 51 and General Fund Allocation

STEP 1a: ACKNOWLEDGED LIST – Measure E Only	
Site Name	Estimated Funding
Northwood ES (Series 2: NC)*	Not eligible
South Lake MS (Series 3A: NC)*	\$557,154
South Lake MS (Series 3A: MOD)	\$4,580,985
Total State Funding Acknowledged	\$5,138,139

^{*}Subject to NC Eligibility

STEP 1b: OPSC WORKLOAD LIST – Measure E Only		
Site Name	Anticipated Funding	
Oak Creek ES (Series AFAP: NC)*	\$452,110	
Total State Funding Anticipated	\$452,110	

^{*}Subject to NC Eligibility



OFFICE OF PUBLIC SCHOOL CONSTRUCTION: STATE GRANTS

Step 2: "Unfunded (Lack of AB 55)" List

- Project applications have been fully reviewed by OPSC staff
- Subject to bi-annual Priority Funding Letter
- Projects funded with General Fund Allocation not subject to Unfunded List or Priority Funding Letter

Step 3: "Apportioned" List

- Project applications that were previously on the Unfunded (Lack of AB 55) list
- Submitted bi-annual Priority Funding Letter
- Shovel-Ready within 90 days of moving to Apportioned list
- Ready for fund Release request funding under Proposition 51 and General Fund


STEP 2: OPSC UNFUNDED LIST – Measure E Only		
Site Name	Amount Approved	
Total State Funded Applications	\$0	

STEP 3: APPORTIONED LIST – Measure E Only	
Site Name	Amount Approved
Total State Funded Applications	\$0





PROGRAM SCHEDULE

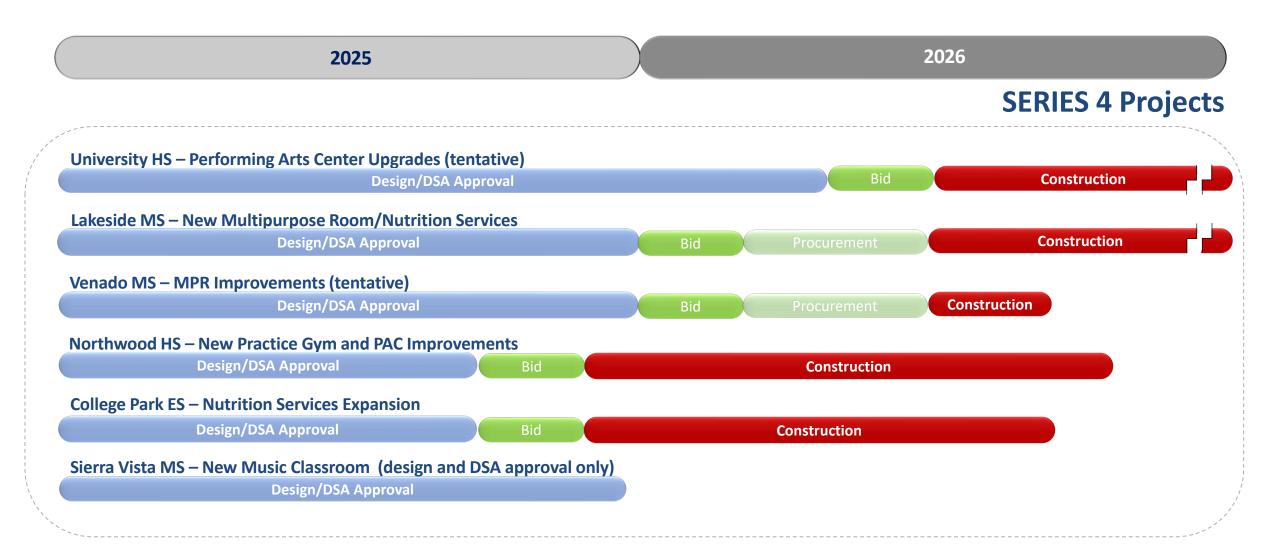





GENERAL ELECTION (NOVEMBER 5, 2024)

SCHOOL BOND MEASURES

- Proposition 2: The Kindergarten through Grade 12 Schools and Local Community College Public Education Facilities Modernization, Repair, and Safety Bond Act of 2024 (58.7% passage)
- K-12 school districts passed 205 of 267 (77% passed)
- Community Colleges passed 14 of 15 (93% passed)

SCHOOL BOND DOLLARS

- Proposition 2: \$10.0 Billion
 - \$8.5 Billion set aside for K-12 school facilities
- K-12 school districts/community colleges: \$45.4 Billion
 - Los Angeles and Orange counties: \$16.8 Billion (37% of statewide bonds in local area)



California School Bond Measures Passed: \$54.4 Billion

2025 CONSTRUCTION MARKET

POTENTIAL CONSTRUCTION MARKET IMPACTS

- Inundation of Bond Projects (11/5/2024 General Election)
 - \$54.4 Billion in bonds
- Recent Wildfires
 - Rebuild in Los Angeles County
- Increase in Tariffs
 - 25% tariff on Mexico and Canada goods
 - 10% tariff on China goods
- Reduction in Workforce Labor
 - Recent changes at Federal level



2025 CONSTRUCTION MARKET


POTENTIAL CHALLENGES FOR SERIES 4 PROJECTS

- Construction Materials
 - Increase costs in materials and supplies
 - Supply chain delays (domestic and foreign)
- Labor
 - Construction labor shortage (skill and unskilled workers)
 - Professional workforce
 - Inexperience and lacking knowledge
- Contributing factors ongoing
 - The Great Resignation (COVID-19 pandemic)
 - Aging Workforce
 - Shrinking pipeline of new workers
 - Working conditions









Measure E Series 3 Project




Street View (Walnut Avenue) - Completed









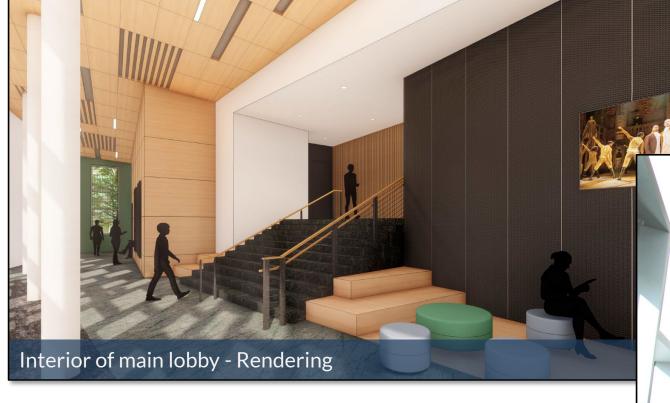



















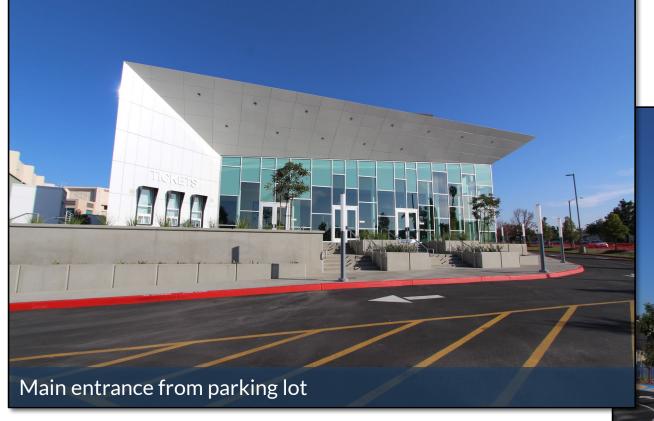

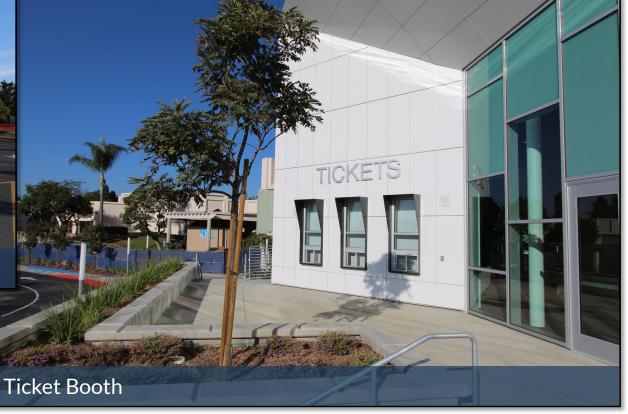













COLLEGE PARK ES (Nutrition Services Expansion)







LAKESIDE MS (New Music Classroom/MPR Improvements/Nutrition)











LAKESIDE MS (New Music Classroom/MPR Improvements/Nutrition)

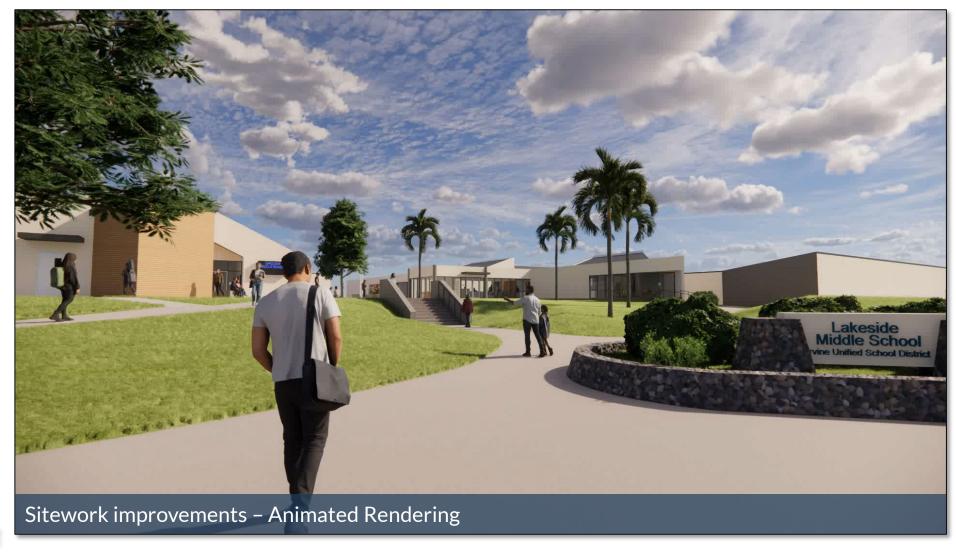





NORTHWOOD HS (New Practice Gym)

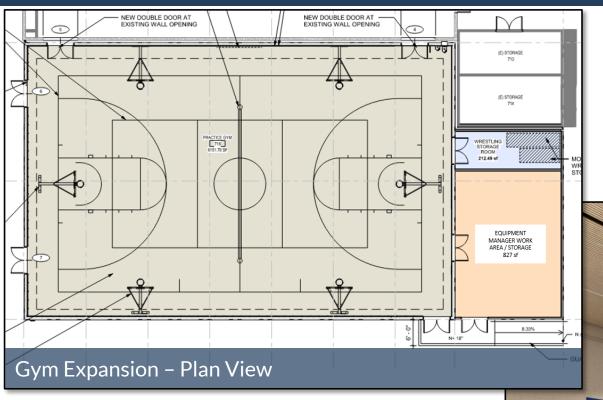








SIERRA VISTA MS (Music Classroom/Nutrition Services)

Existing MPR will be converted to a music classroom and expanded Nutrition Services area (Phase 3 and Phase 4).

Series 4 includes the design phase and DSA approval.

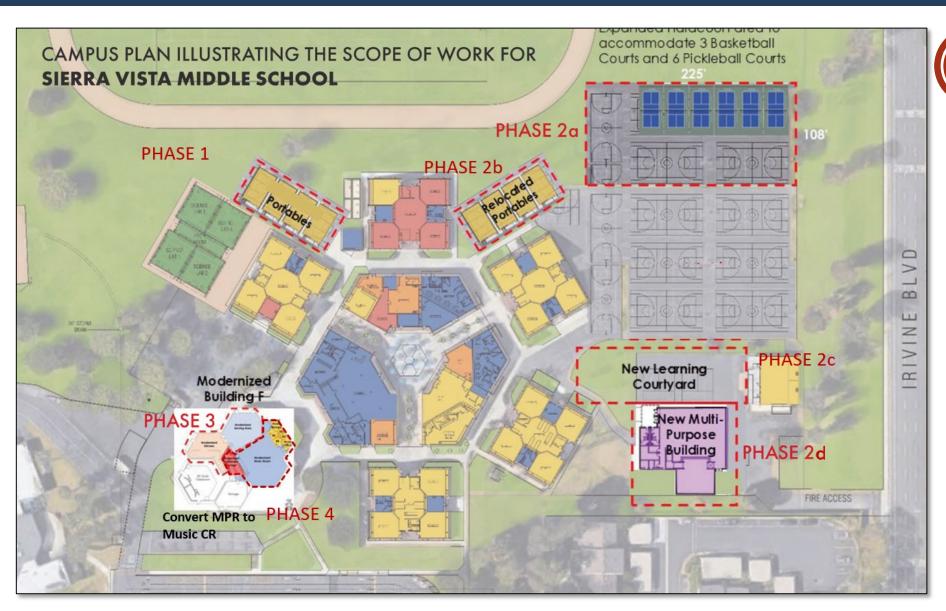



REMAINING SERIES 4 PROJECTS

- University HS (Performing Arts Center Improvements)
 - Design Phase
 - Developing conceptual plans and program
 - Reviewing building siting options
- Venado MS (MPR Improvement)
 - Programming Phase refining scope of work





QUESTIONS

NEXT MEETING

April 28, 2025 at 6:30pm

Location: TBD

