

Westwood Basics Interim School Public Information Meeting

October 11, 2017



MEETING AGENDA

- Introductions
- Overview of Measure E Program
- Project Overview
- Transportation Logistics
- Resources Background
- Questions and Answers



INTRODUCTIONS

- Kim Coffeen – IUSD, Director Facilities Planning
- Robert Ramirez– IUSD Planner, Facilities Planning

Additional Team Members:

- Kelvin Okino – IUSD, Executive Director, Facilities Planning and Construction
- Astrid Ramirez– IUSD, Principal of Brywood ES
- Annie Brown – IUSD, Public Information Officer
- Matthew Nicholson, Architect, Ruhnau Ruhnau Clarke



Overview of Measure E Program



MEASURE E

- **Measure E: School Facilities Improvement Measure**
- **\$319 million bond to upgrade older schools within the District**
- **Voter approved in June 2016**
- **Includes 28 schools within the Irvine Unified School District**




MEASURE E PROJECTS

 - High Schools 5

 - Middle Schools 5

 - Elementary Schools 18

28

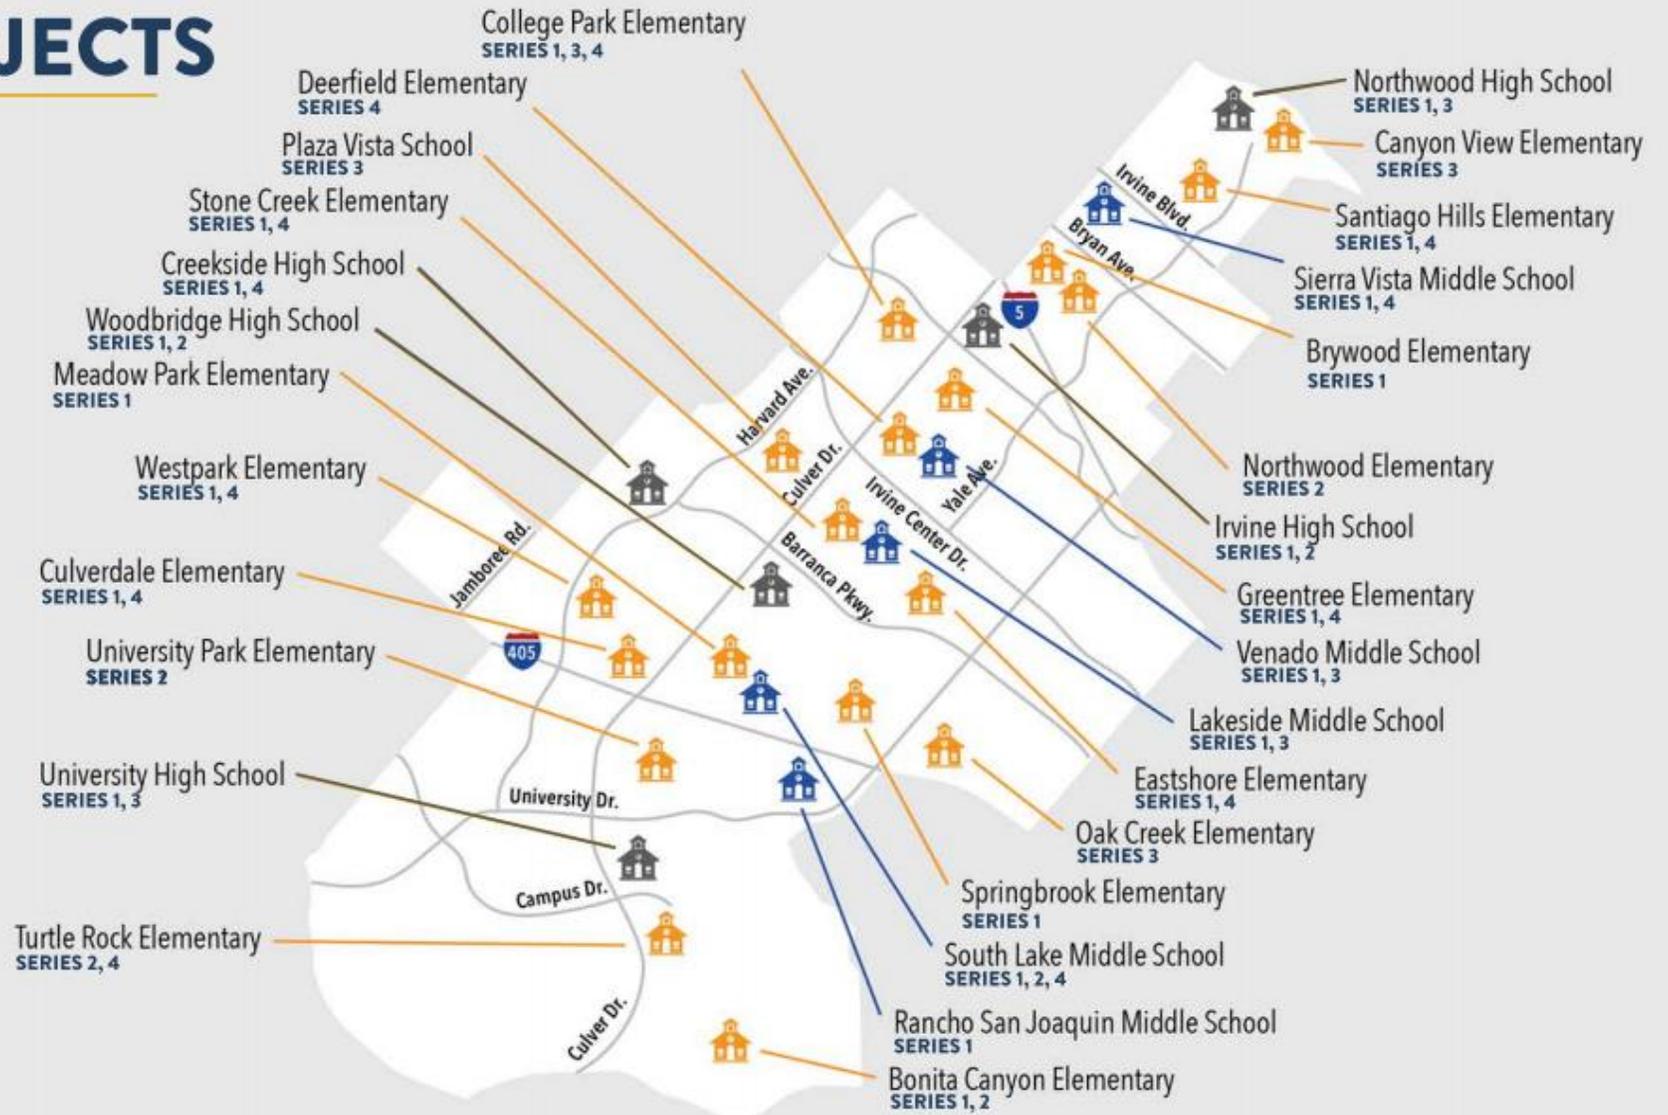

SERIES 1 PRIORITIES

- **Safety and security**
 - Install interior doors at elementary school classrooms
- **Age of the school site**
 - Modernize eligible schools over 25 years old
- **Projects that will impact the greatest amount of students**
 - Projects for high schools and middle schools, which benefit most Irvine USD students, who will attend these schools
- **Upgrade Science Labs at middle schools**



Project Overview



PROJECT SCOPE

Westwood Interim Campus

- 5 New portable classrooms and restroom facility
- Renovation of the existing building
- Replacement of kinder playground equipment & restoration of play area
- Move in of Brywood Park July 2018
- Removal of Portables Summer 2019




SITE PLAN



SITE PLAN

New Relocatable Restroom Building



5 New Relocatable Buildings

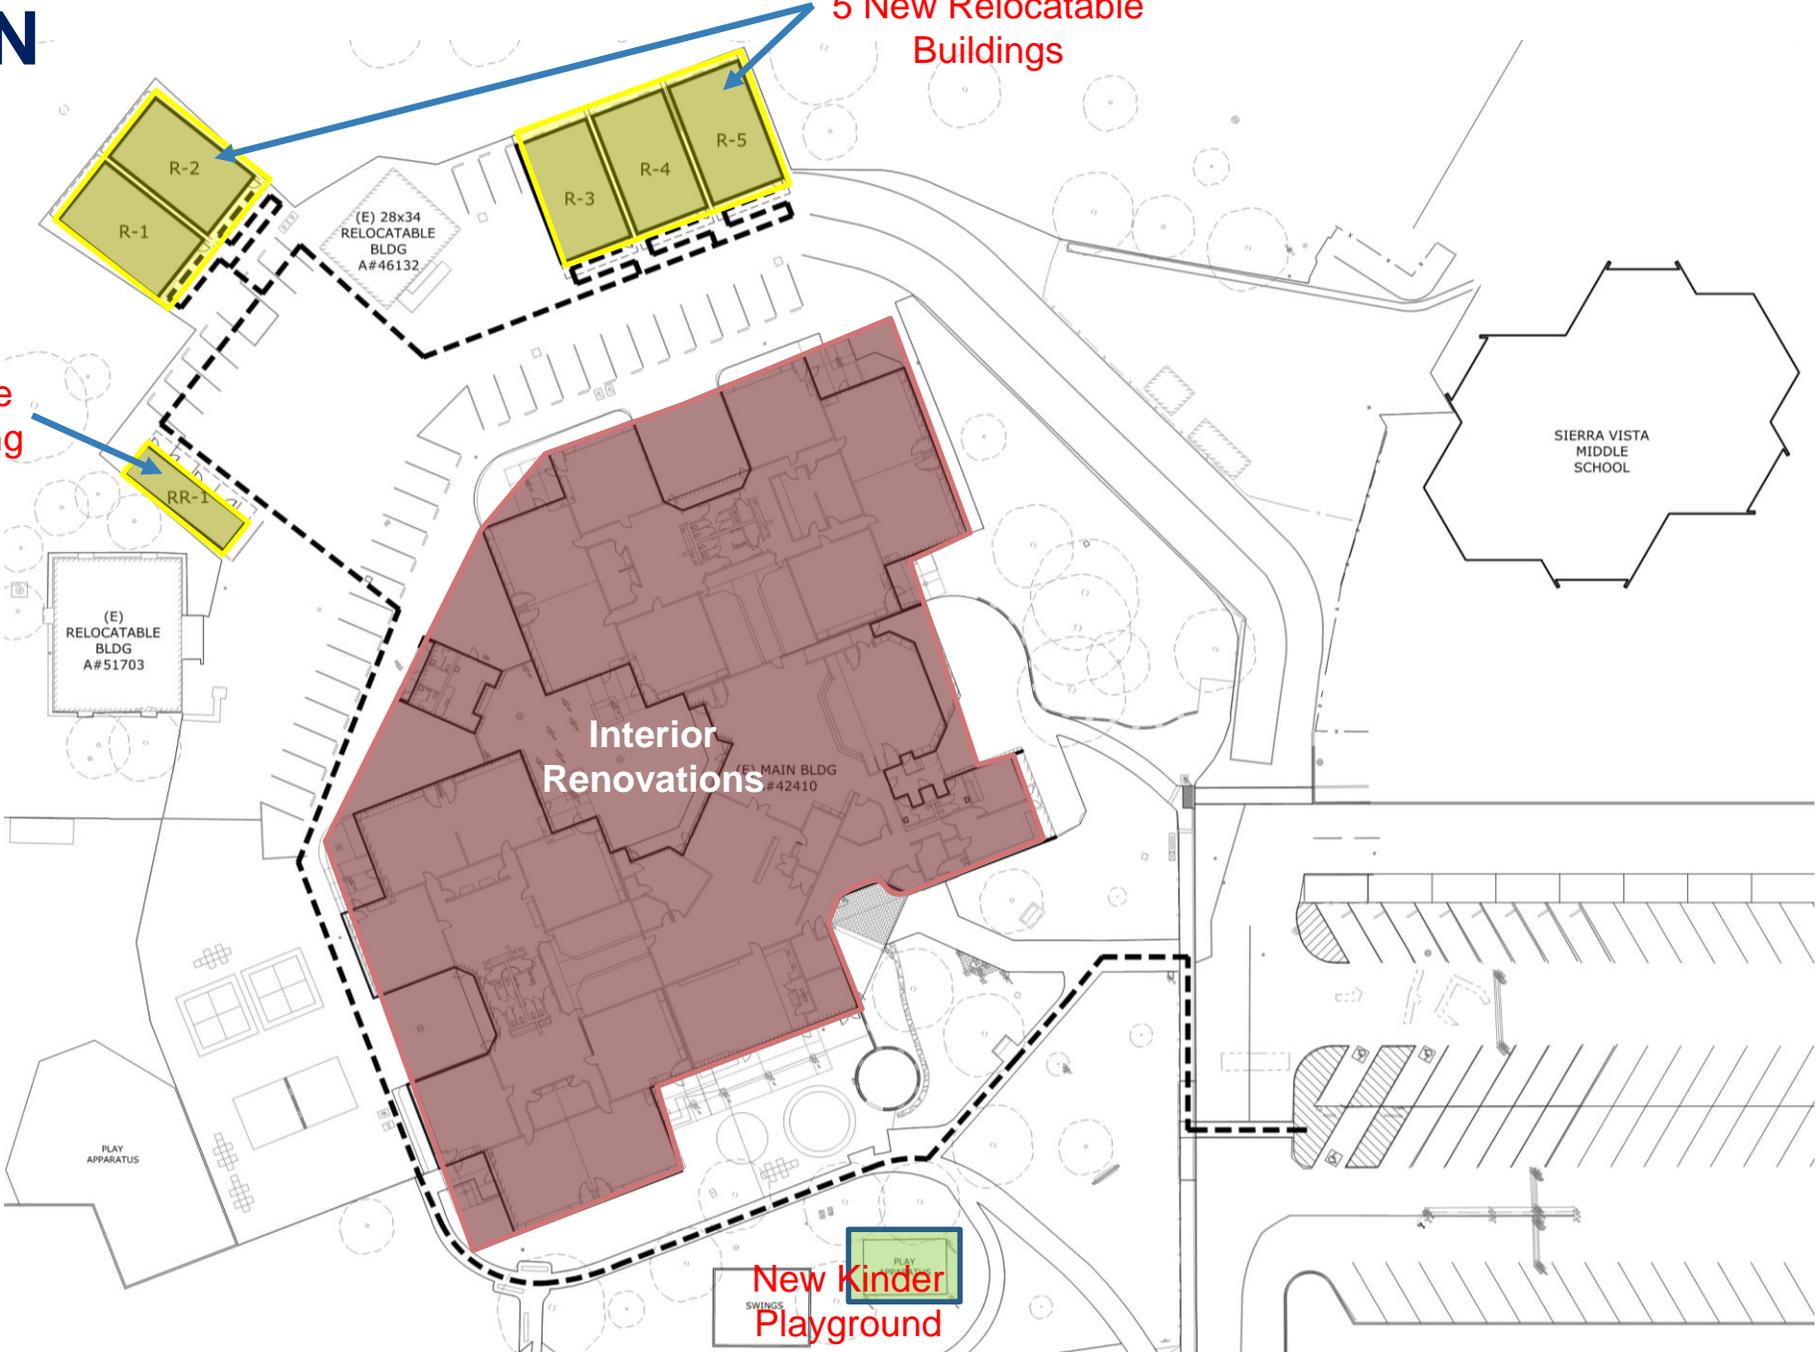


New Kinder Playground



FLOOR PLAN

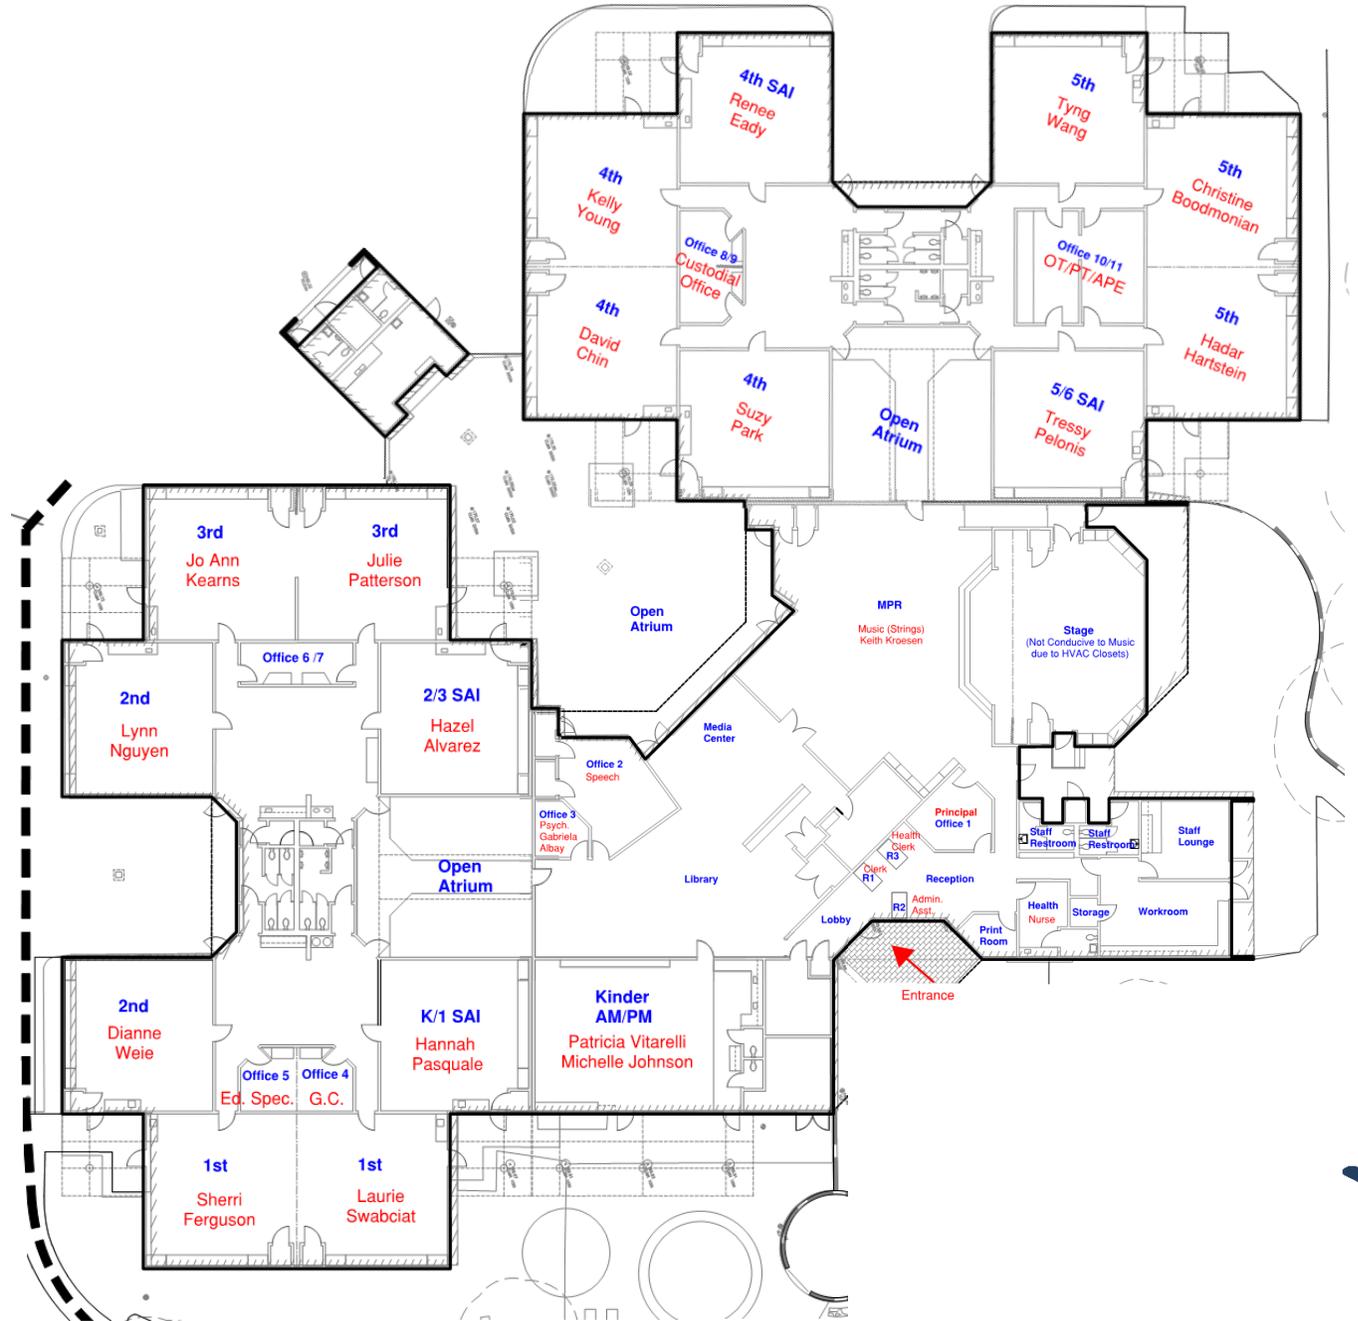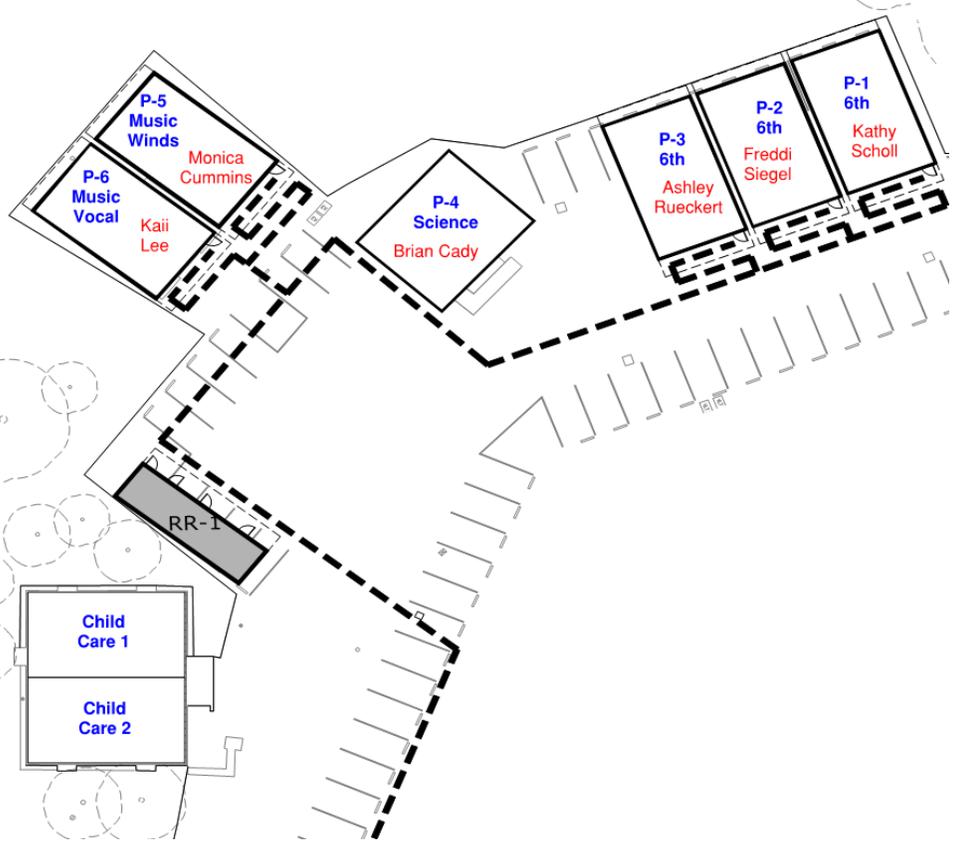

PROJECT MILESTONE SCHEDULE

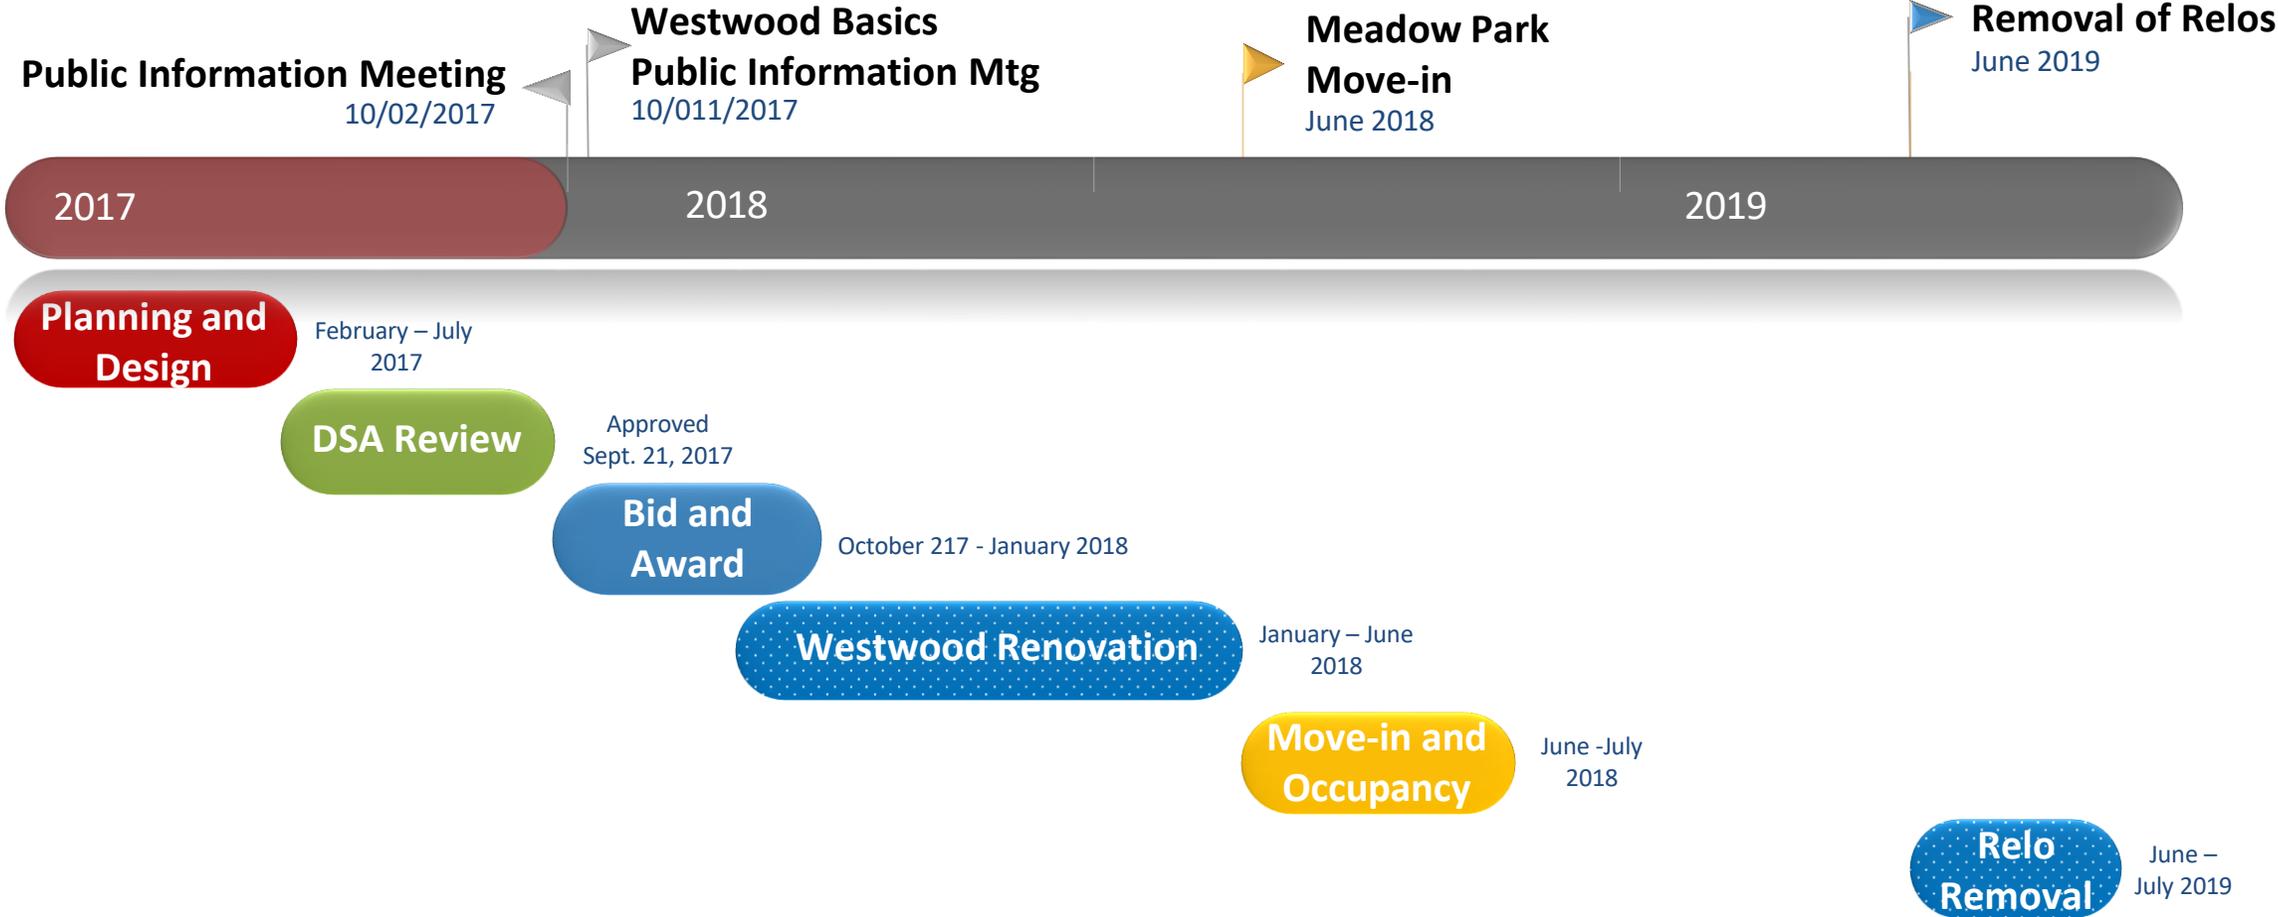

PROJECT PLANNING

MEETINGS

- 10/11/17 Traffic Logistics Meeting with City of Irvine and Irvine PD
- 10/3/17 School Site Coordination
- 8/9/10 Project Review City of Irvine and Irvine PD
- 5/23/17 Project Review Principal
- 5/17/17 I.T. Technology Coordination
- 5/1/17 Food Services Coordination
- 5/1/17 M&O Scope of work Review



Transportation Logistics



TRANSPORTATION LOGISTICS

Transportation Options

- Walking routes to school
- Brywood parking open for drop-off
- Bike rack location
- Staggered start schedule
- Communication with parents



SITE PLAN



MEASURE E RESOURCES

- Measure E Webpage
iusd.org/MeasureE
- Brywood Measure E Webpage – school site updates
iusd.org/MeasureEbw
- Citizens Oversight Committee Webpage
iusd.org/COC
- Contact Email for Questions/Concerns
MeasureE@iusd.org





QUESTIONS and ANSWERS
